Knoxville CSD 20-012

Weekly Report #1 Week of 6/07/2021

Prepared By

Andrew Paleczny		apaleczny@boydjones.biz

Project Summary:

- Temporary fence has been installed around the project site.
- We have completed rough grading the site, installing SWWPP protection, and installing the building pad.
- We have completed the underground utilities under the west parking.
- We have begun underground electrical and plumbing in the building pad.
- We have begun over excavation for exterior building foundations.
- MEP trades have mobilized.

The following items were completed during the week of June 07, 2021:

- Demo continued in the high school..
  - We continued ceiling demo, removed CMU in the kitchen, and began demoing out the floor for the new freezer.
  - We continued removing piping, ductwork, and mechanical equipment through phase 3.
  - We poured back concrete where the old freezer/cooler was located.
- Middle School work
  - We poured footings for Area B along gridline 2, 3, R, and U.
  - We began excavating footings for Area C along gridline C-7 and C-8.
  - We installed underground plumbing for water fountain into high school weight room.

The following items are scheduled for the week of June 14th, 2021:

- Demo to continue in high school into phase 3 and phase 4.
- We will continue demoing out the floor for the new kitchen freezer/cooler.
- We will continue removing pipe, ductwork, and mechanical units.
- We will be installing CMU wall in-fills and patches in the kitchen.
- We will continue excavating and pouring footings in Area C.
- We will be excavating footings in Area B/C along gridline T.
- We will be installing the storm sewer lines in Area B.
- We will be completing the installation of utilities near the west parking lot area.

Progress Pictures

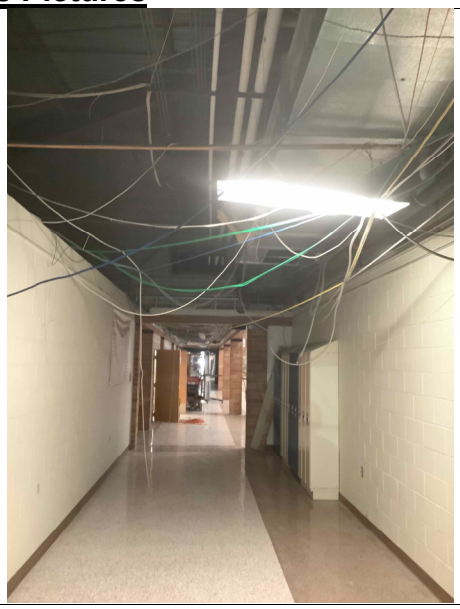

Fig. 1: High School Phase 3 Demo.

Fig. 2: High School Kitchen Concrete Pour Back.

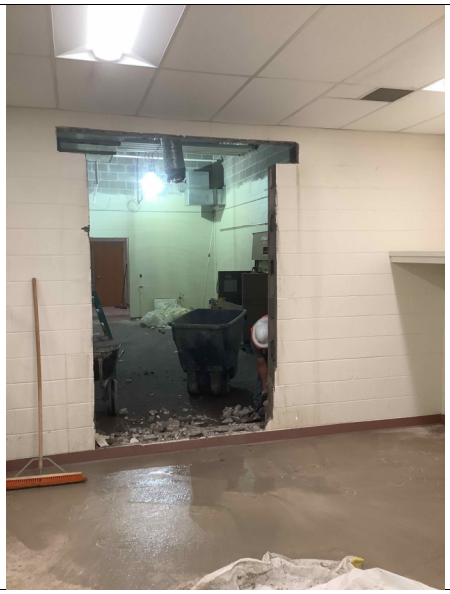

Fig. 3: High School Kitchen CMU Demo.

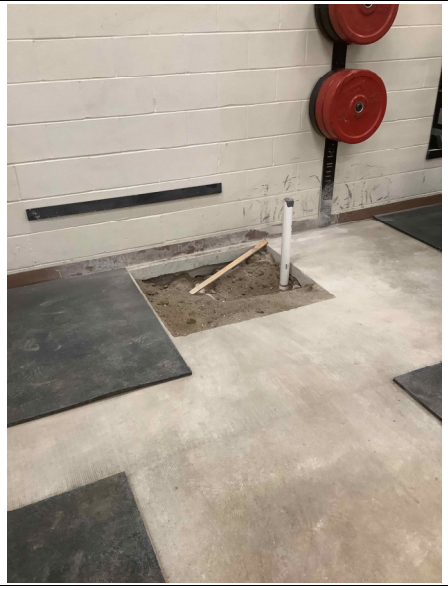

Fig. 4: High School Weight Room U/G Plumbing Rough-In.

Fig. 5: Middle School Area B Footing.

Fig. 6: Middle School Area C Footing Prep.
